Noble County

State of Indiana

ADA

Transition Plan

Sidewalk – Ramp Data

January 30, 2013

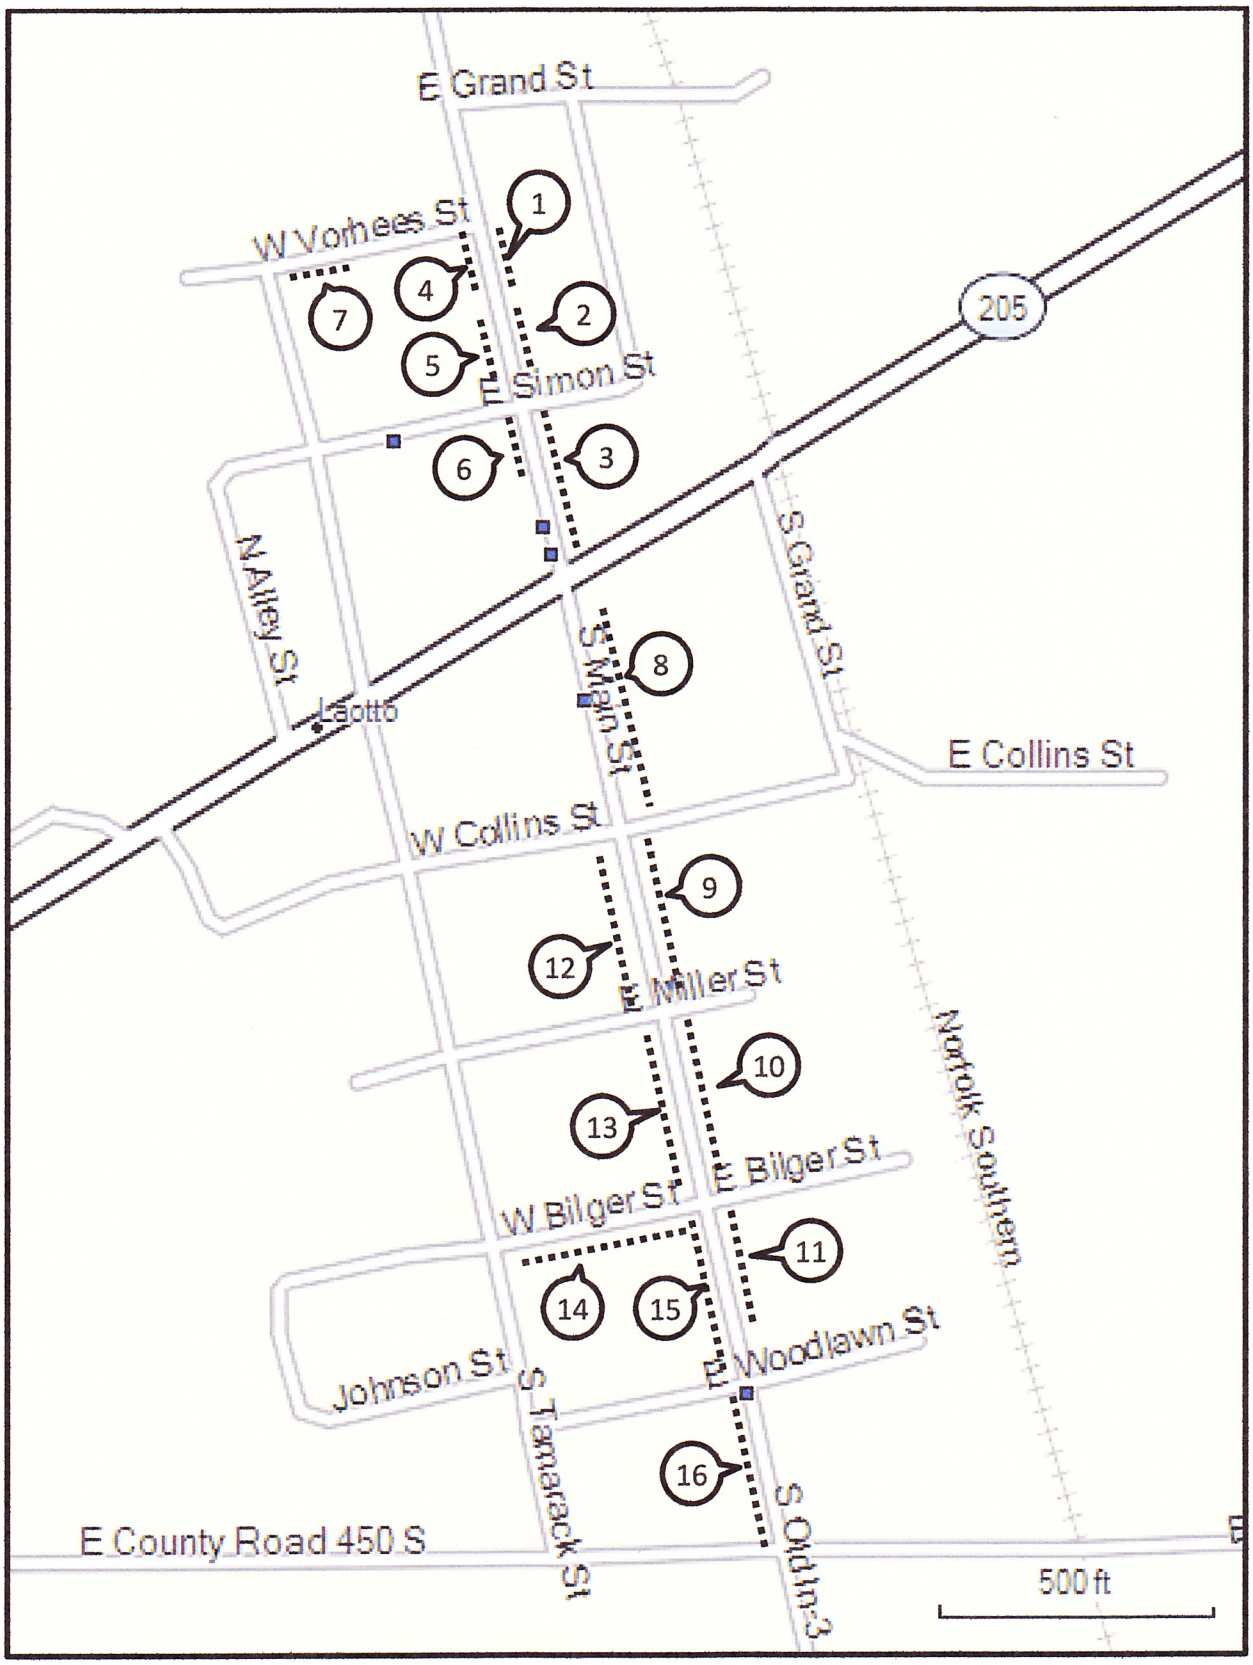

LAOTTO SIDEWALKS – RAMP MAP

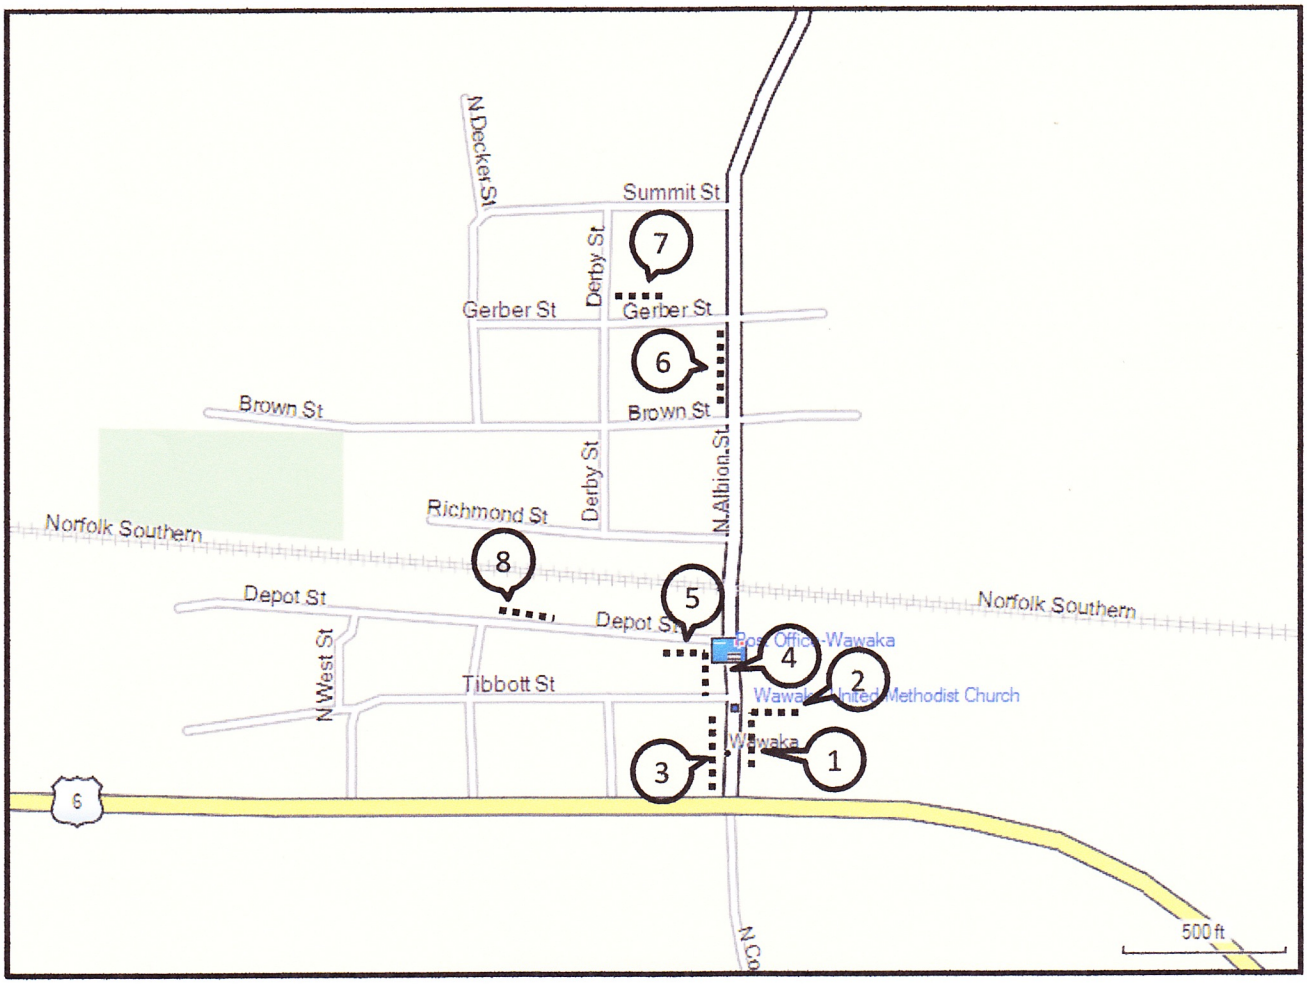

WAWAKA SIDEWALK – RAMP MAP

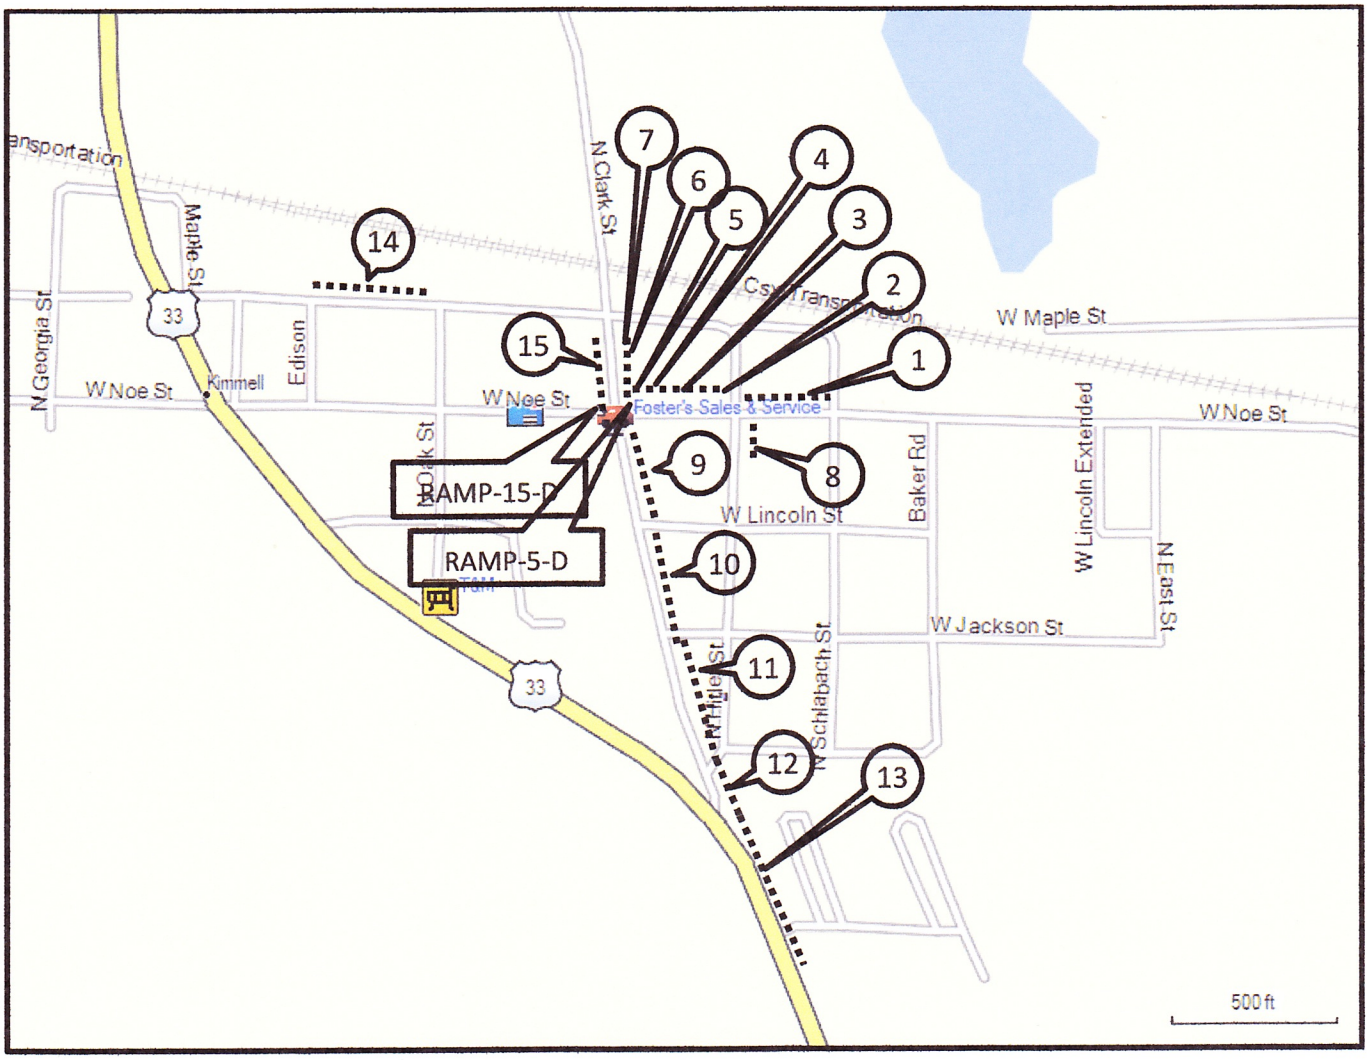

KIMMELL SIDEWALK – RAMP MAP

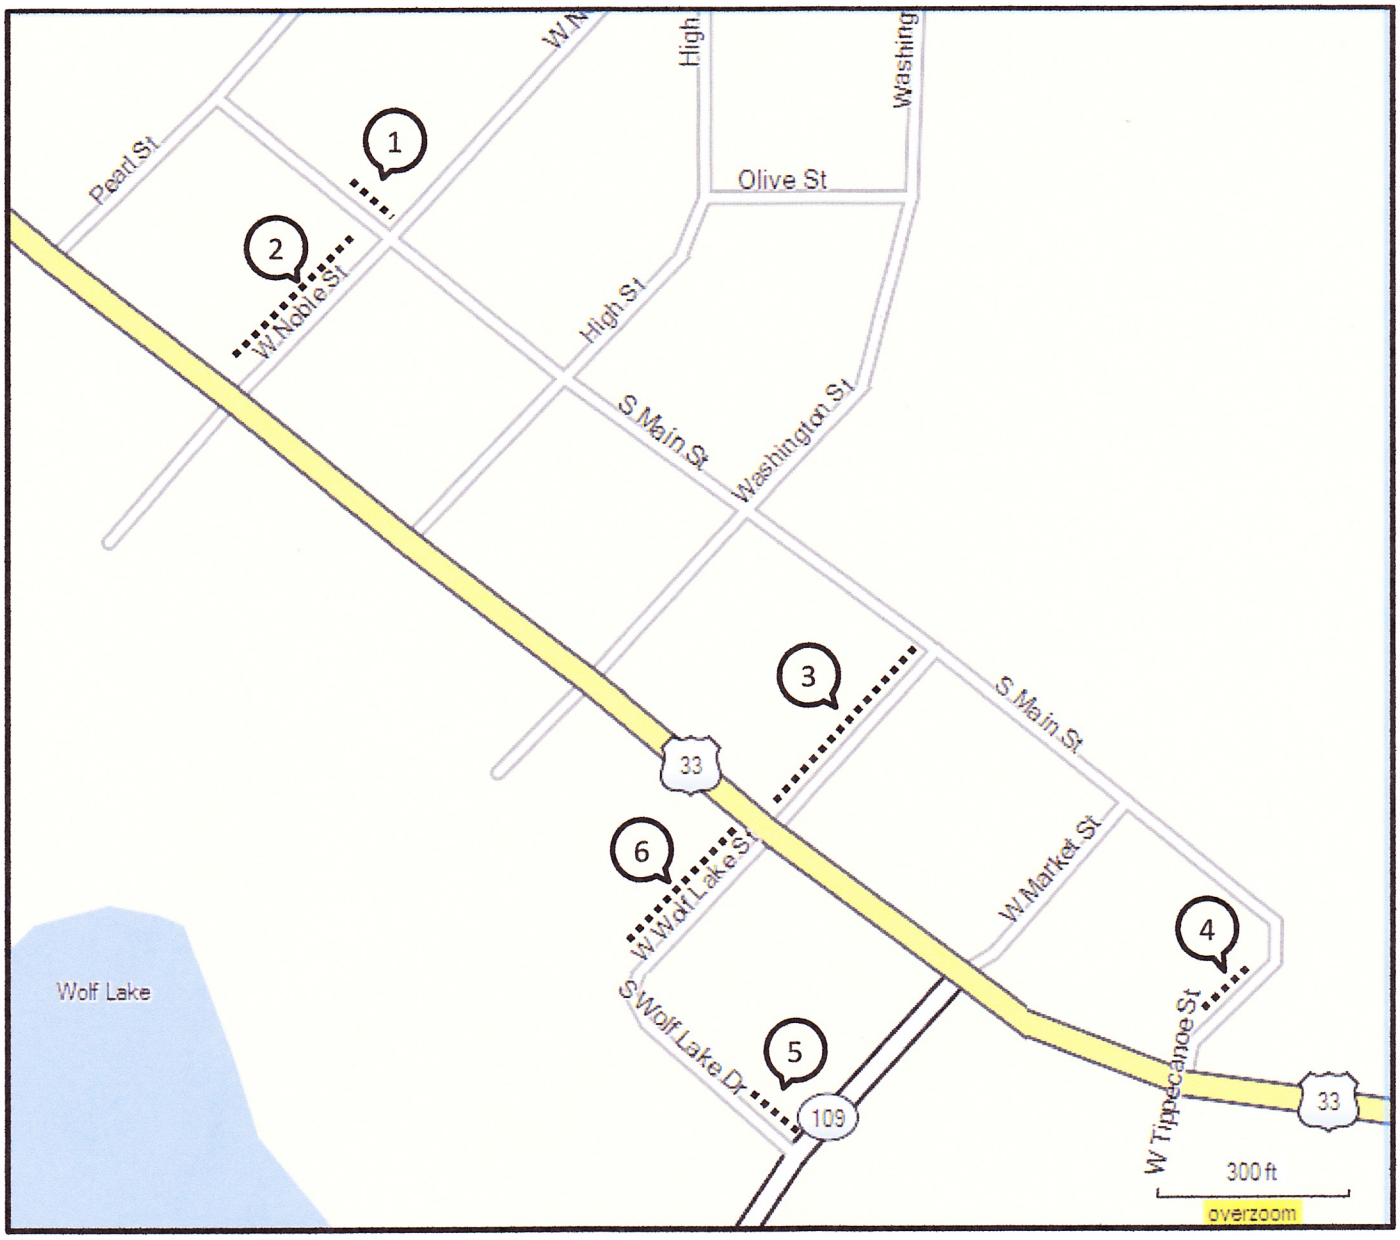

WOLFLAKE SIDEWALK – RAMP MAP

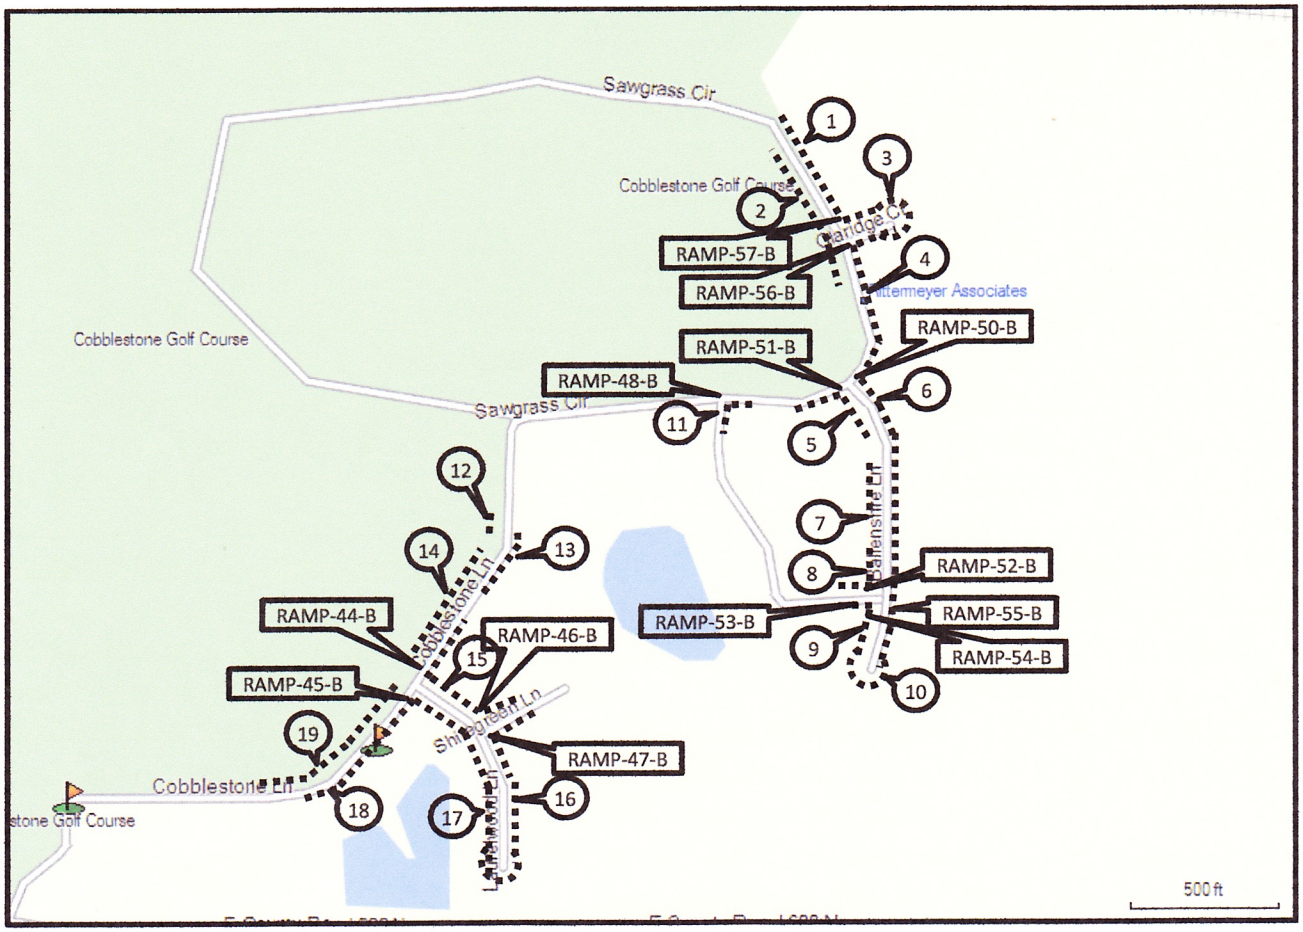

COBBLESTONE ADDITION SIDEWALK –RAMP MAP

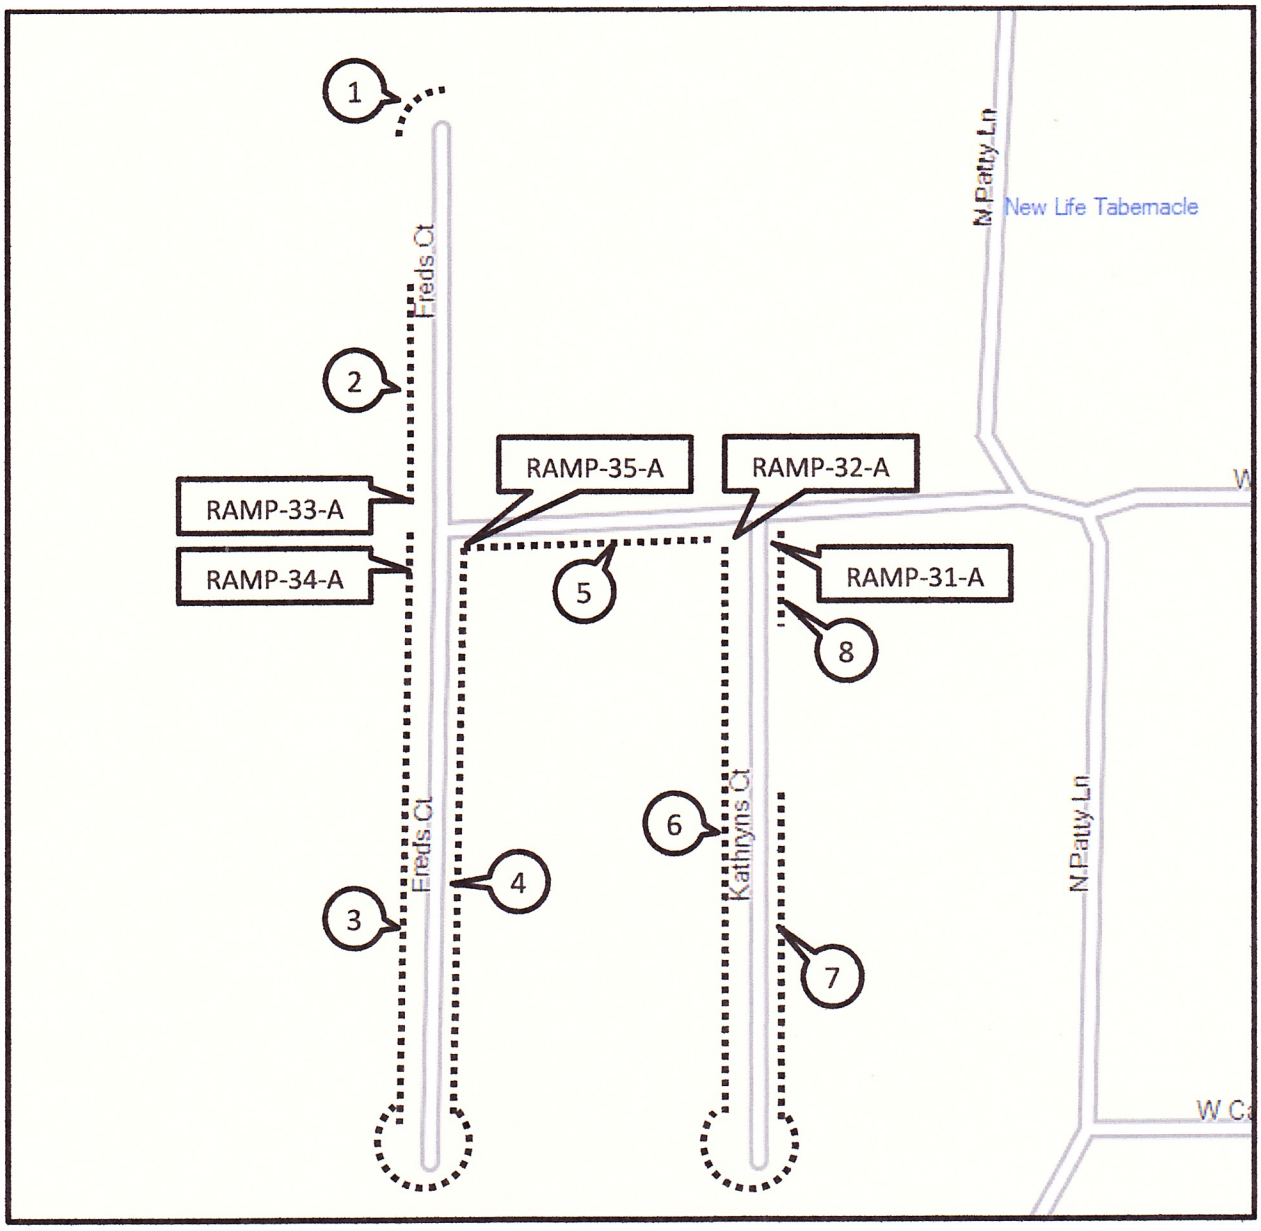

MEADOW LANE SIDEWALK – RAMP MAP

NOBLE COUNTY SIDEWALK-RAMP SURVEY DATA

January 30, 2013

Row#	Location	Area	Length	Width	Condition	Area (SqYd)
1	LaOtto	1	167	3	D	55.67
2	LaOtto	2	167	3	D	55.67
3	LaOtto	3	283	3	D	94.33
4	LaOtto	4	167	3	D	55.67
5	LaOtto	5	167	3	D	55.67
6	LaOtto	6	52	3	A	17.33
7	LaOtto	7	84	2	A	18.67
8	LaOtto	8	418	4	C	185.78
9	LaOtto	9	320	4	D	142.22
10	LaOtto	10	334	3	D	111.33
11	LaOtto	11	266	3	D	88.67
12	LaOtto	12	290	4	C	128.89
13	LaOtto	13	336	3	C	112.00
14	LaOtto	14	133	3	D	44.33
15	LaOtto	15	333	3	C	111.00
16	LaOtto	16	260	3	C	86.67
17	Wawaka	1	119	6	A	79.33
18	Wawaka	2	99	6	A	66.00
19	Wawaka	3	210	5	D	116.67
20	Wawaka	4	118	4	D	52.44
21	Wawaka	5	153	5	D	85.00
22	Wawaka	6	330	5	D	183.33
23	Wawaka	7	50	5	D	27.78
24	Wawaka	8	65	2	A	14.44
25	Kimmell	1	251	4	C	111.56
26	Kimmell	2	155	5	C	86.11
27	Kimmell	3	100	5	A	55.56
28	Kimmell	4	36	6	D	24.00
29	Kimmell	5	79	6	D	52.67
30	Kimmell	6	63	4	A	28.00
31	Kimmell	7	118	4	C	52.44
32	Kimmell	8	77	3	D	25.67
33	Kimmell	9	320	3	D	106.67
34	Kimmell	10	320	3	D	106.67
35	Kimmell	11	400	3	D	133.33
36	Kimmell	12	165	3	D	55.00
37	Kimmell	13	430	3	D	143.33
38	Kimmell	14	434	3	D	144.67
39	Kimmell	15	235	6	D	156.67
40	Wolflake	1	70	4	A	31.11
41	Wolflake	2	290	4	A	128.89
42	Wolflake	3	278	4	D	123.56
43	Wolflake	4	70	2	A	15.56
44	Wolflake	5	70	3	C	23.33
45	Wolflake	6	71	3	A	23.67
46	Wolflake	7	232	3	C	77.33

Row#	Location	Area	Length	Width	Condition	Area (SqYd)
47	Cobblestone	1	200	5	A	111.11
48	Cobblestone	2	140	5	A	77.78
49	Cobblestone	3	300	5	A	166.67
50	Cobblestone	4	350	5	A	194.44
51	Cobblestone	5	295	5	A	163.89
52	Cobblestone	6	300	5	A	166.67
53	Cobblestone	7	60	5	A	33.33
54	Cobblestone	8	210	5	A	116.67
55	Cobblestone	9	345	5	A	191.67
56	Cobblestone	10	140	5	A	77.78
57	Cobblestone	11	200	5	A	111.11
58	Cobblestone	12	100	5	A	55.56
59	Cobblestone	13	190	5	A	105.56
60	Cobblestone	14	290	5	A	161.11
61	Cobblestone	15	610	5	A	338.89
62	Cobblestone	16	390	5	A	216.67
63	Cobblestone	17	500	5	A	277.78
64	Cobblestone	18	350	5	A	194.44
65	Cobblestone	19	380	5	A	211.11
66	Cobblestone	Ramp 44	8	5	B	4.44
67	Cobblestone	Ramp 45	8	5	B	4.44
68	Cobblestone	Ramp 46	8	5	B	4.44
69	Cobblestone	Ramp 47	8	5	B	4.44
70	Cobblestone	Ramp 48	8	5	B	4.44
71	Cobblestone	Ramp 50	8	5	B	4.44
72	Cobblestone	Ramp 51	8	5	B	4.44
73	Cobblestone	Ramp 52	8	5	B	4.44
74	Cobblestone	Ramp 53	8	5	B	4.44
75	Cobblestone	Ramp 54	8	5	B	4.44
76	Cobblestone	Ramp 55	8	5	B	4.44
77	Cobblestone	Ramp 56	8	5	B	4.44
78	Cobblestone	Ramp 57	8	5	B	4.44
79	Meadow Ln	1	80	5	A	44.44
80	Meadow Ln	2	170	5	A	94.44
81	Meadow Ln	3	515	5	A	286.11
82	Meadow Ln	4	500	5	A	277.78
83	Meadow Ln	5	240	5	A	133.33
84	Meadow Ln	6	500	5	A	277.78
85	Meadow Ln	7	380	5	A	211.11
86	Meadow Ln	8	70	5	A	38.89
87	Meadow Ln	Ramp 33	8	5	A	4.44
88	Meadow Ln	Ramp 34	8	5	A	4.44
89	Meadow Ln	Ramp 35	8	5	A	4.44
90	Meadow Ln	Ramp 32	8	5	A	4.44
91	Meadow Ln	Ramp 31	8	5	A	4.44
